

# WR-ALC Offline Scanning Project Status

03/24/2004

Lucent Technologies



# Background and Brief History

- ✓ Contract Award: 30Sept2001
- ✓ Started Scanning one shift November 01, 2001
- ✓ Full production with one shift, W/E December 7, 2001.
- ✓ 2nd shift in production, W/E January 11, 2002.
- ✓ Initial projected completion 31Dec2004 (38 months).
- ✓ Expected to be finished 30Apr2004 (31 months).

# Project Scanning Progression

<u>Cards (in Millions)</u>	<u>Date Scanned</u>	<u>Date Transferred</u>
1	March 8, 2002	March 26, 2002
2	May 21, 2002	June 11, 2002
3	August 9, 2002	
4	October 24, 2002	
5	January 16, 2003	
6	April 8, 2003	October 2003
7	July 25, 2003	
8	September 18, 2003	
9	December 16, 2003	
10	March 22, 2004	9,515,923
10.4	April 21, 2004	

Legend: Black = Completed; Red = Projected

# Current Status

**Total Cards in WR Repository: 10,400,000\***

**As of 03/12/2004:**

- **Total Cards Scanned: 9,977,144**
- **Total Cards Transferred: 9,515,923**
- **Estimated Number of cards to be scanned: 422,856**
- **Estimated Number of Cards to be transferred: 884,077**

\* Based on measurements of remaining cards in repository  
in mid-February

## Conditions for Scheduled Completion


- ❖ Number of scan personnel will remain constant
- ❖ There are no major, long term hardware failures
- ❖ Lucent will require 2 to 3 weeks after scan completion for wrap-up

# Wrap-Up Activities

- ✓ Push Remaining Images Up to JEDMICS RAID
- ✓ Update ACATSS with Final TRL Files
- ✓ Generate Final MEDALS Input
- ✓ Pack up, Cleanup and Ship Out


# Progress Status

**Scan Production - Cumulative**  
**01 April 2003 to 31 March 2004**

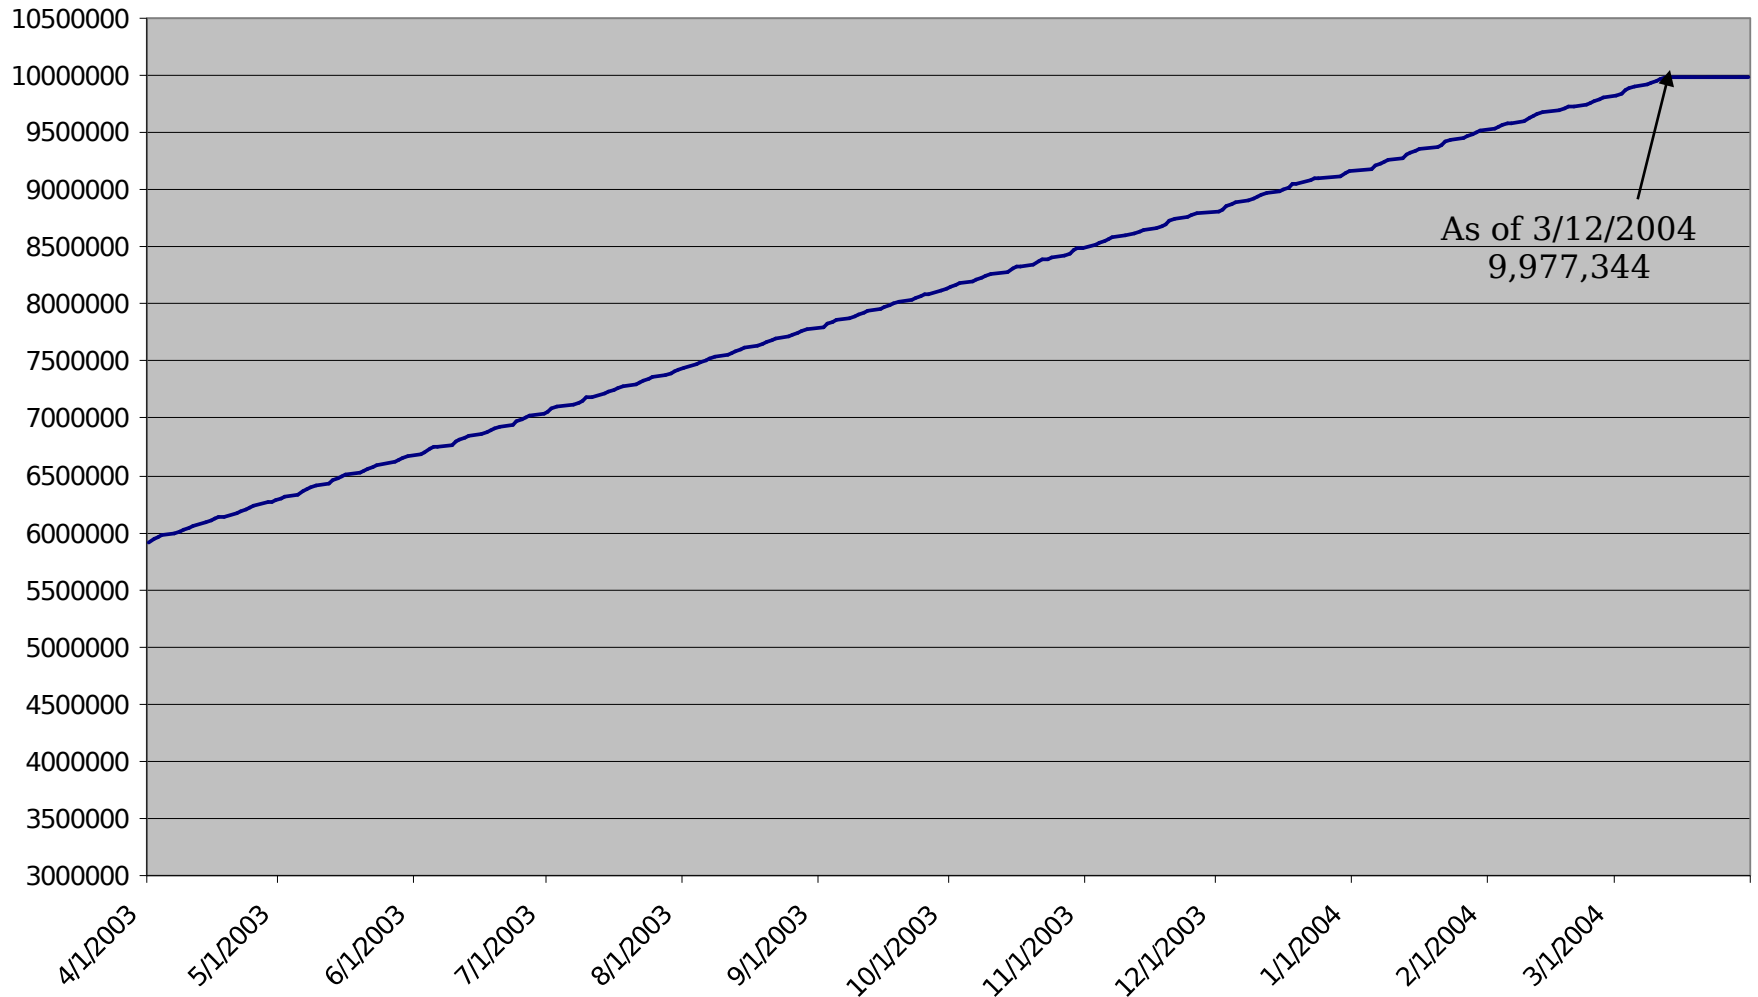

# Progress Status

**Scan Production - Target VS Actual**  
**01 April 2003 to 31 March 2004**

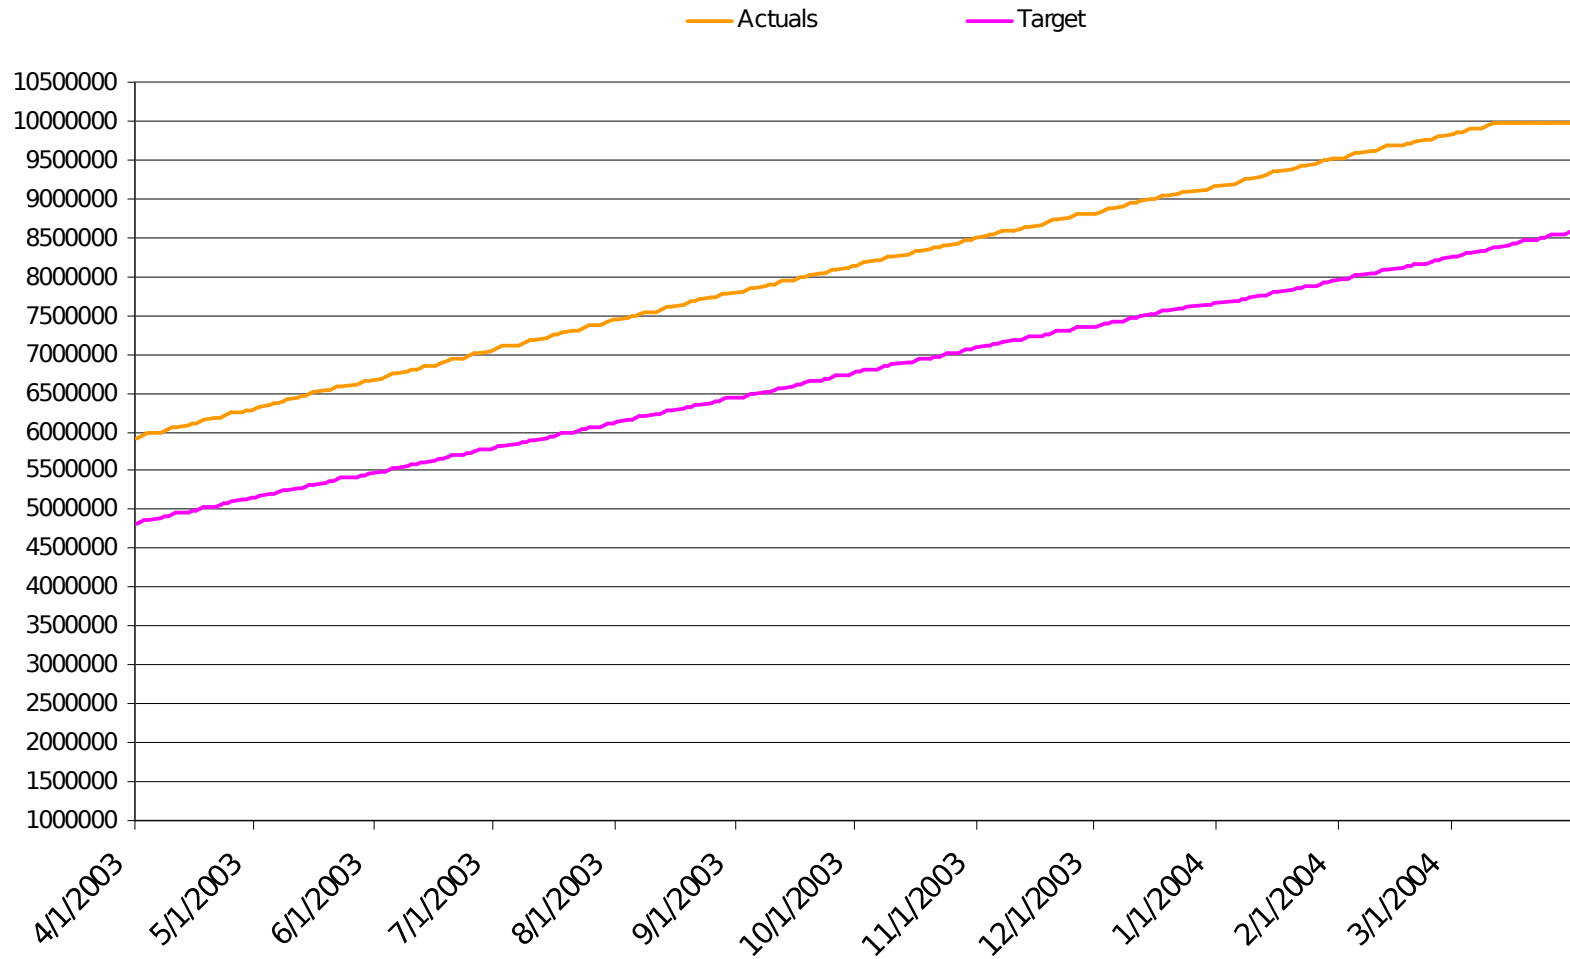




# Progress Status


## Cumulative J EDMICS Data Transfer 07 Mar 2003 - 29 Feb 2004

— CumulativeTotal — Target

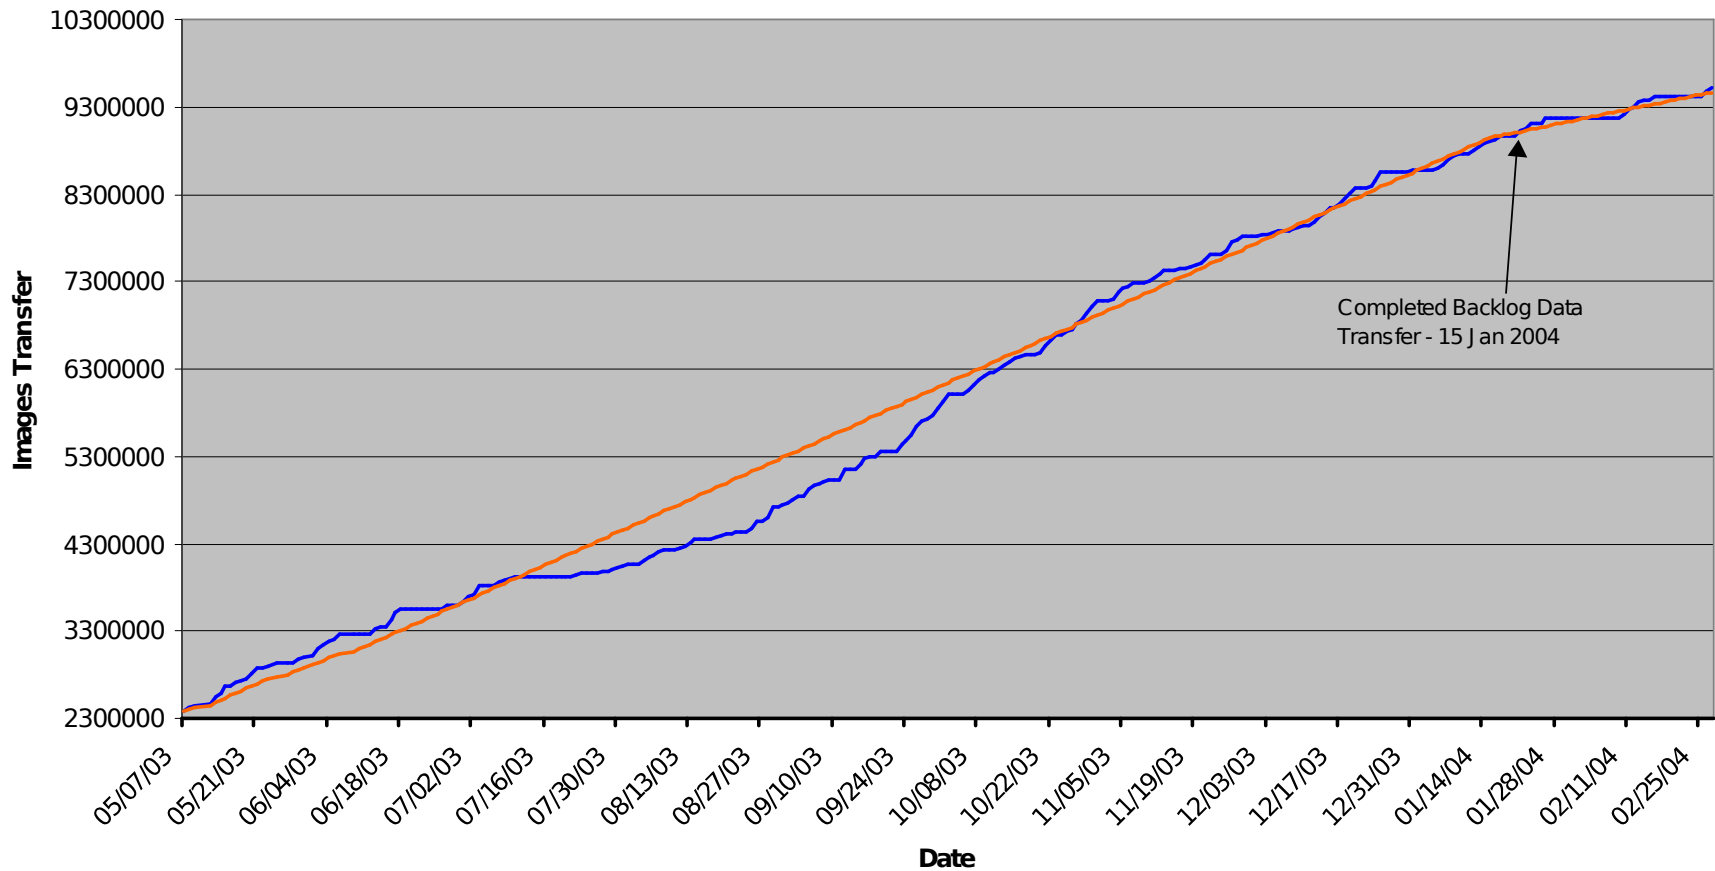


# Progress Status

**Total QA Review Images**  
**01 April 2003 to 31 March 2004**

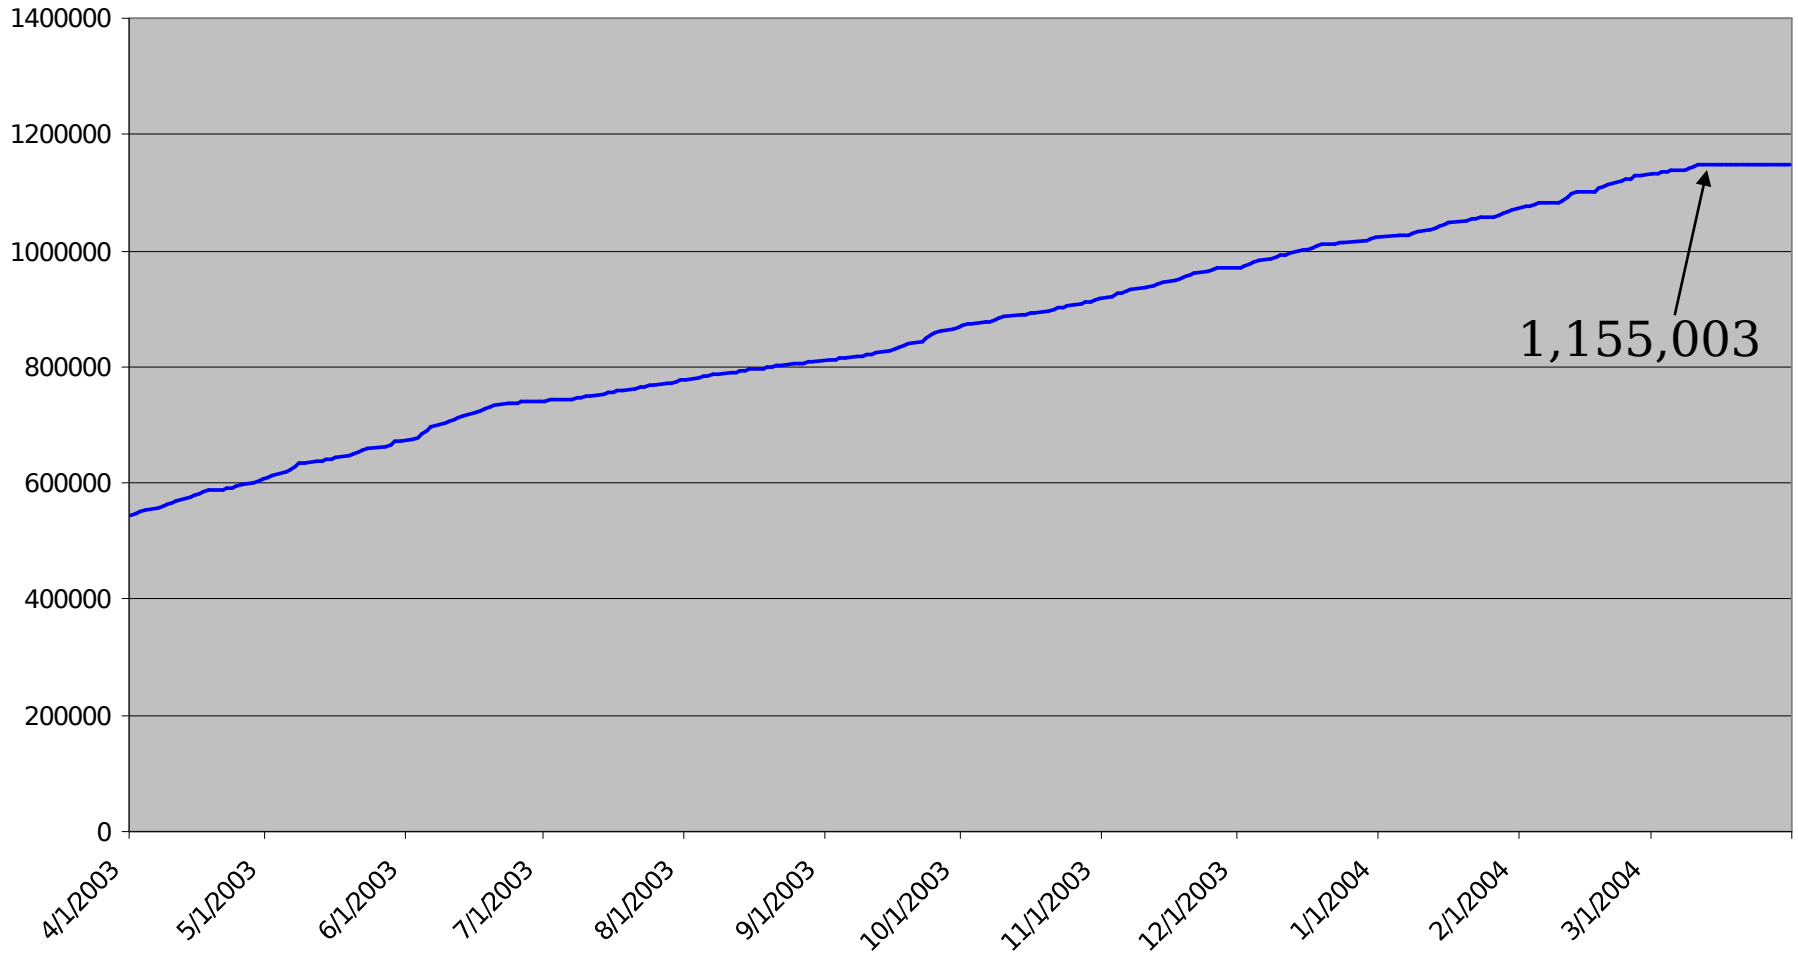

# Progress Status


**QA-Review & Reject % of Total Scanned**  
**01 April 2003 to 31 March 2004**

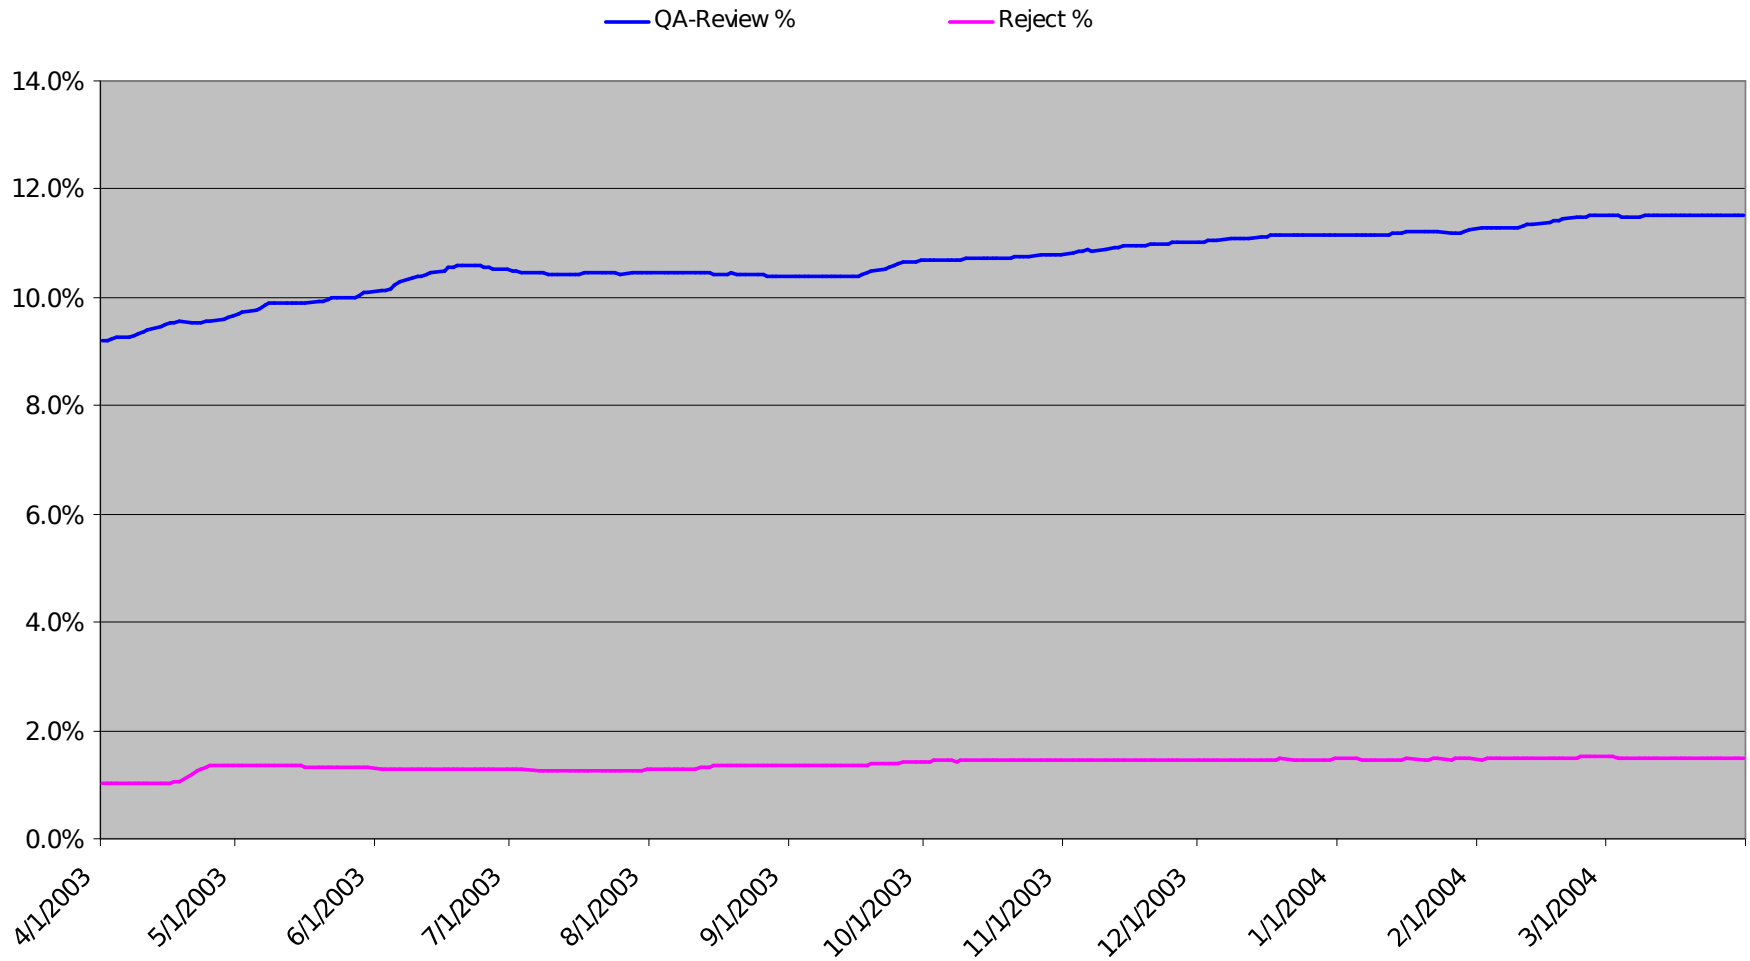

# Progress Status

**Total QA-Reviews per Shift**  
**01 April 2003 to 31 March 2004**

— 1st-Rev      — 2nd-Rev

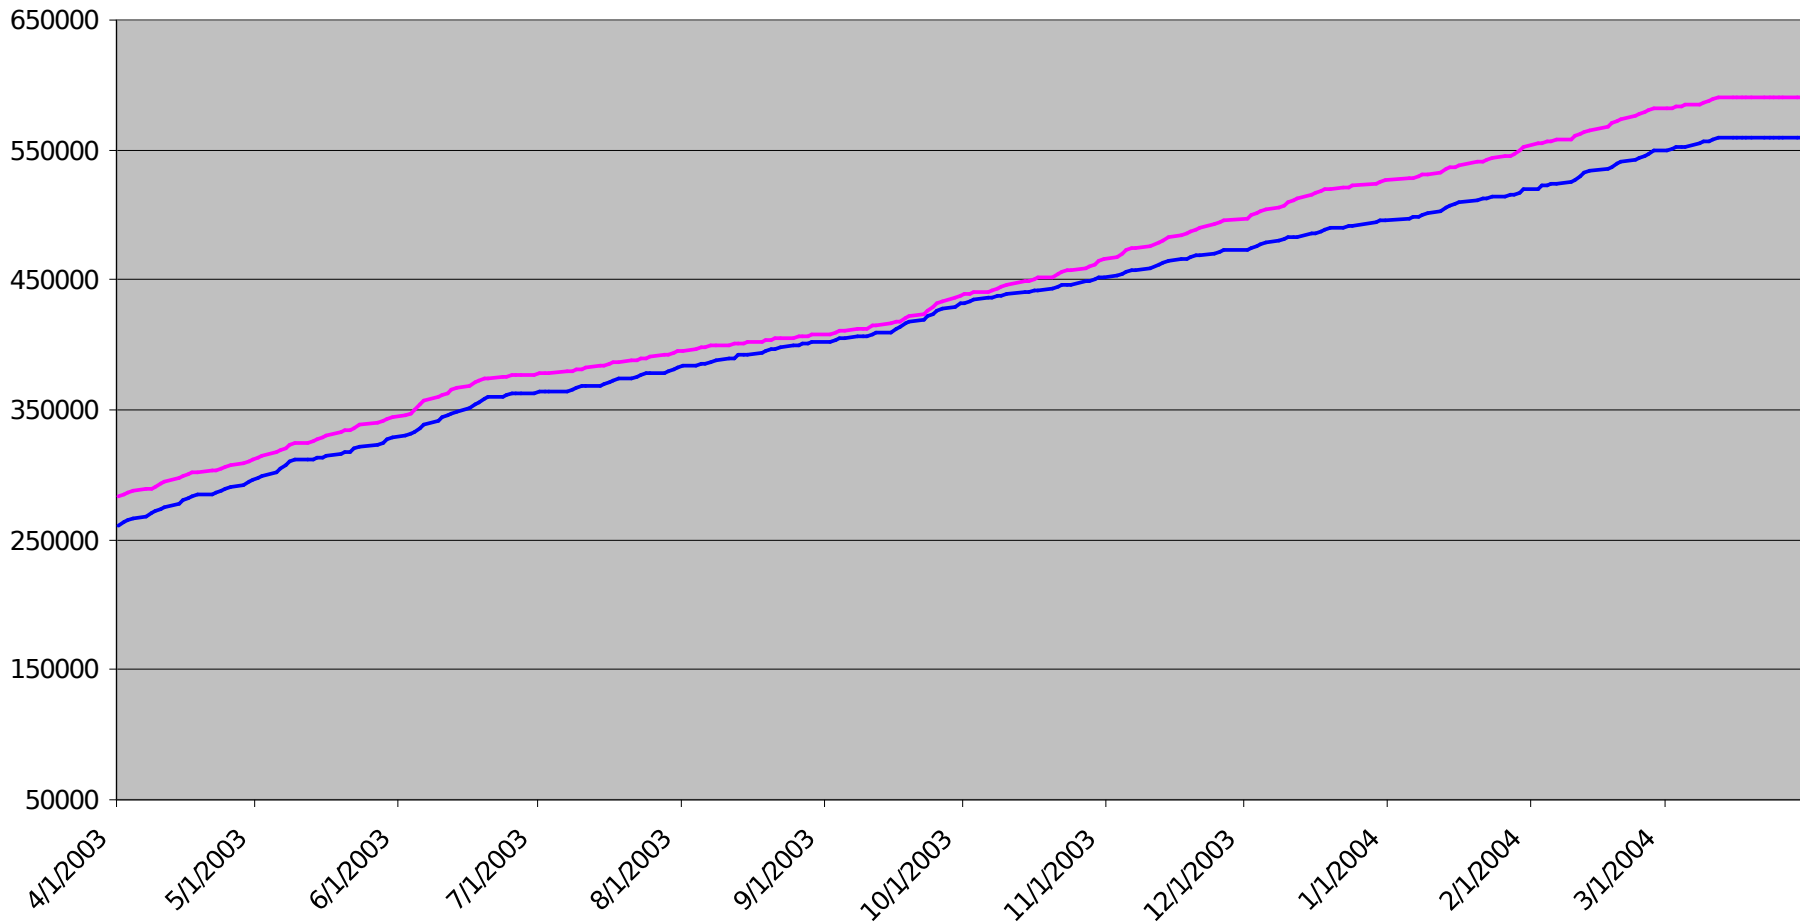



Progress Status

Questions?

Comments?
